

**July 8, 2022**

**To:** Chris Hammond

**CC:** Jeff Downs, Doug Bright

**Job Name:** BBCHS HVAC UPGRADES

**Job Number:** 21311

**Address:** 700 W. North St. Bradley, IL 60915

**Project Manager:** Jim Brown

**General Superintendent:** Ryan Brown

**Carpenter Foreman:** John Teders

---

**Overview:**

- Wire tray installation
- Electrical wiring
- Duct Installation
- Pipe Installation
- Duct/Pipe Insulation
- Ceiling Installation
- Sprinkler pipe installation
- Temperature control rough in

**Manpower On Site**

- **CM Team**
- Johnson Downs 3
- **Prime Contractors**
- Ruder Electric 8
- Glade 3
- Johnson Downs 8
- M&M 4
- Illini Fire Service 4
- JC Insulation 2
- Otto Baum 2
- Tatro Painting 1
- **Total Effort: 35**

**Weather:**

Seasonal Temperature / Overcast


**Look Ahead:**

- RTU Delivery

**Important Dates:**

- RTU Start-up August 8, 2022

**Glazed Tile Patching**

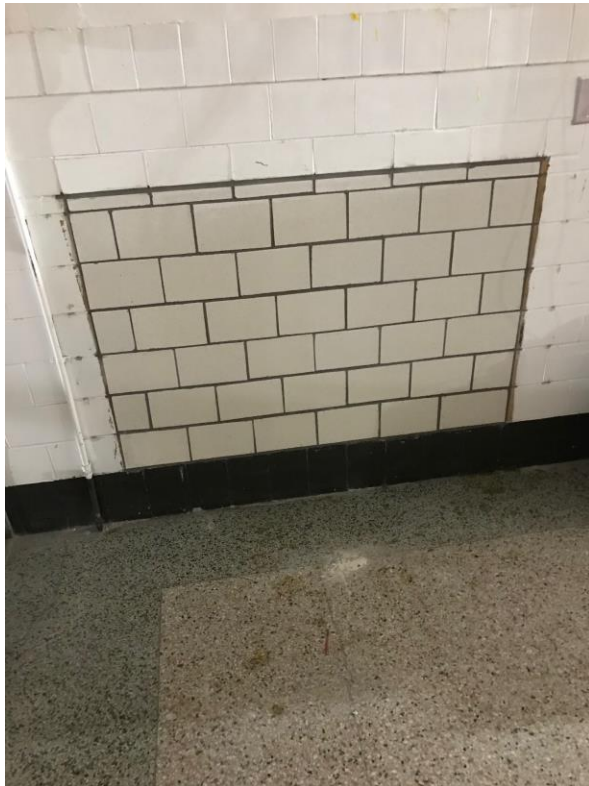

Ceiling Border Tile



New Light Fixture



Sprinkler Head Ceiling Tile




Classroom Wire Mold Receptacle



Fire Alarm Wiring




Panel Wiring

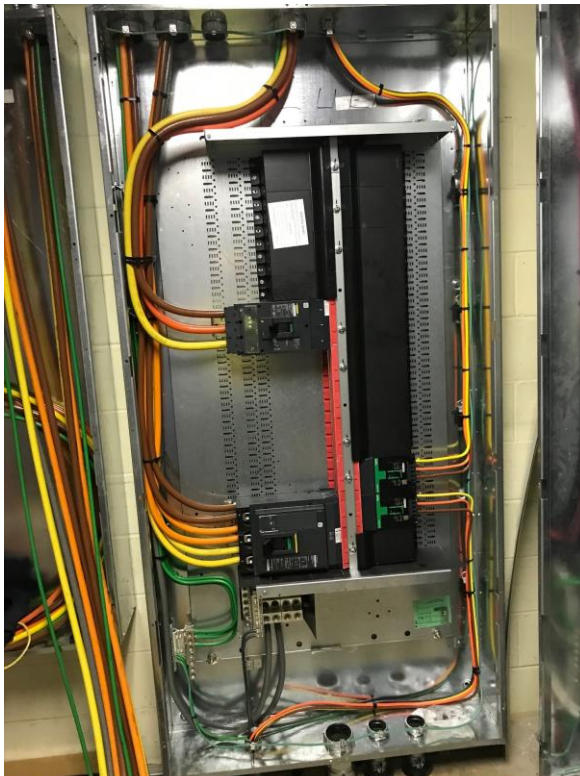



Panel Wiring

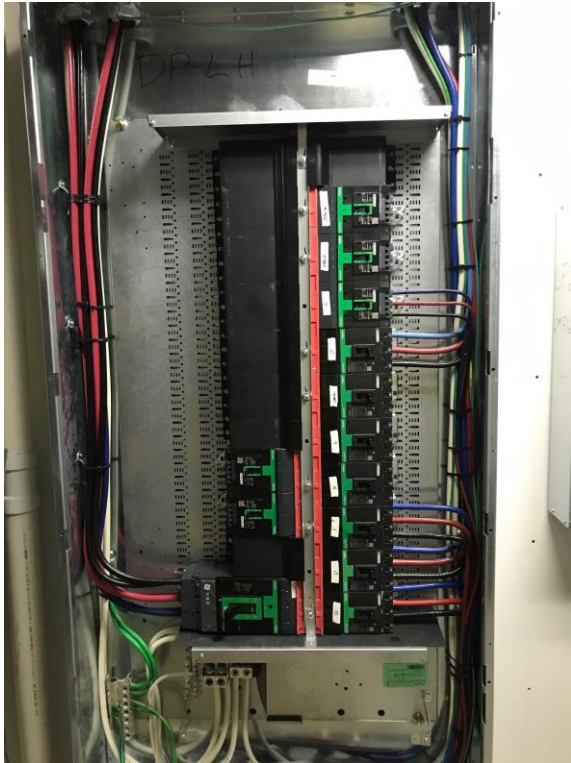

Painted Drywall



### Pipe Labeling



### Wire Tray

