

July 28, 2023

To: Chris Hammond,

CC: Ryan Fredricks, Jeff Downs, Doug Bright,

Job Name: Bourbonnais Bradley Community High School

Job Number:

Address: 700 W. North Street, Bradley IL 60915

Project Manager: Jim Brown

Superintendent: JR Woods

Project Engineer: Brian Nelson

Overview:

- Ceiling Grid Installation continues.
- HVAC Ductwork Installation continues.
- Electrical Conduit Installation continues.
- Ceiling Tile Installation continues.

Contractors on Site:

- Johnson Downs: 10 Trades
- Ruder Electric: 5 Electrician
- Knotts Masonry: 5 Masons
- M&M Sheet Metal: 5 Trades
- Matco Fire Protection: 2 Trades
- Trane: 2 Trades

Total: 29 trades on site this week

Weather:

HOT/Humid

Look Ahead:

- RTU 1 Delivery
- AHU 1 Start Up
- MEP Trims

Inspections:

- N/A

Milestones:

Finished Floor

Pictures:



Ceiling Grid & Tile Installation



Finished Floor Prep



Finished Floor Leveling




New Ductwork & Insulation



Ready for RTU 1



HVAC Casser Installed in Ceiling

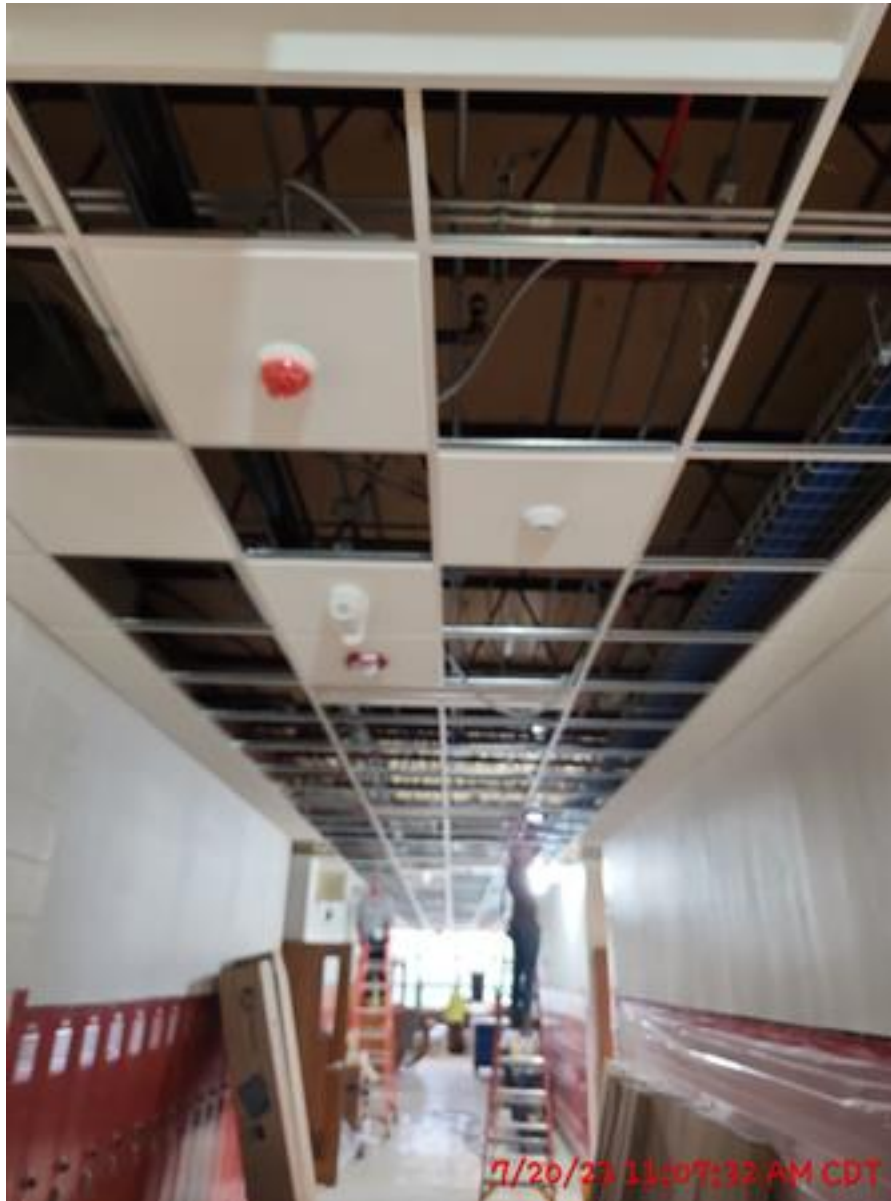

Fire Alarm Devices Installed
