



**August 11, 2023**

**To:** Chris Hammond,

**CC:** Ryan Fredricks, Jeff Downs, Doug Bright,

**Job Name:** Bourbonnais Bradley Community High School

**Job Number:**

**Address:** 700 W. North Street, Bradley IL 60915

**Project Manager:** Jim Brown

**Superintendent:** JR Woods

**Project Engineer:** Brian Nelson

---

**Overview:**

- Ceiling Tile
- RTU 1 Delivery and Lift
- Clean Up
- Demobilization

**Contractors on Site:**

- Johnson Downs: 5 Carpenters
- Glade: 4 Plumbers/Pipe Fitters
- Ruder Electric: 5 Electricians
- Knotts Masonry: 2 Masons
- M&M Sheet Metal: 5 Sheet Metal Workers
- Matco Fire Protection: 7 Tradesmen
- Trane: 4 Tradesmen
- Tatro: 1 Painter
- **Total: 33 tradesmen on site this week**

**Weather:**

Seasonal

**Look Ahead:**

- Fire Alarm Programming
- RTU 1 Start Up
- Air & Hydronic Balancing

**Inspections:**

- N/A

**Milestones:**

RTU 1 Landed

**Pictures:**



RTU 1 Delivery & Rigging

Instillation of Rooftop Unit




RTU 1 Set on Curb



Completed Classroom



Furniture Installed

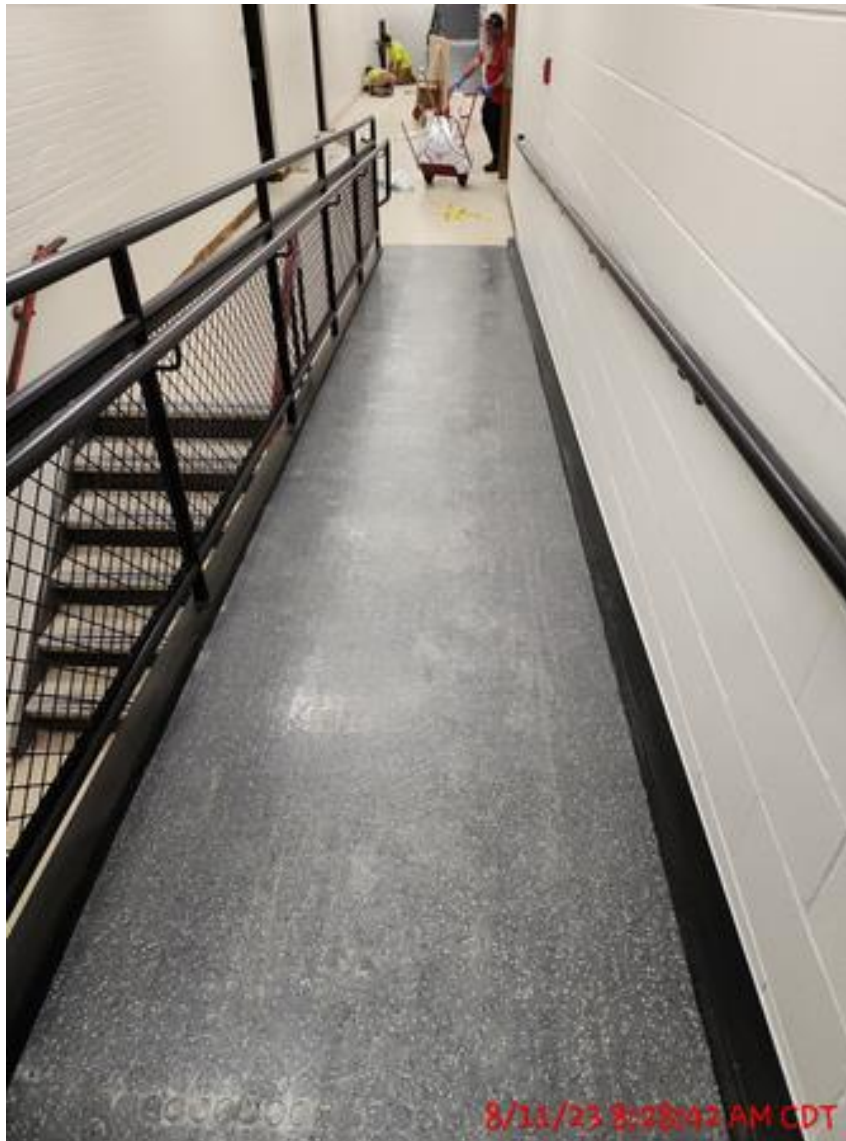

Completed ADA Ramps





MEP Trims



NW Classroom Completed





Furniture Installed NW Classroom



NW Second Floor Corridor



Painting the Ramp Handrail
